


**MARINA 1 REPLACEMENT
 BID NO. 3536
 WATER AND LAND SIDES CONCURRENT**

ID	Task Name	Duration	Start	Finish
0	Project Schedule	521 days	Mon 12/1/08	Tue 7/13/10
1	LANDSIDE DESIGN	131 days	Mon 12/1/08	Thu 4/30/09
2	Restart Project	1 day	Mon 12/1/08	Mon 12/1/08
3	ABR	18 days	Mon 12/1/08	Fri 12/19/08
4	Building & Safety Approval	106 days	Fri 12/19/08	Thu 4/23/09
5	Review & Approve Final Plans & Specifications	7 days	Thu 4/23/09	Thu 4/30/09
6	Design Complete	0 days	Thu 4/30/09	Thu 4/30/09
7	FUNDING	45.25 days	Fri 5/8/09	Wed 7/1/09
8	DBAW Staff Report and Loan Docs	1 day	Fri 5/8/09	Fri 5/8/09
9	DBAW Commission Hearing	1 day	Tue 5/19/09	Tue 5/19/09
10	CAR for Loan Docs	26 days	Fri 5/8/09	Tue 6/9/09
11	Funding Available	0 days	Wed 7/1/09	Wed 7/1/09
12	CONTRACT	69 days	Thu 4/30/09	Mon 7/20/09
13	Advertise Bid Number 3536	23 days	Thu 4/30/09	Thu 5/28/09
14	Receive Bids	0 days	Thu 5/28/09	Thu 5/28/09
15	Review Bids	9 days	Thu 5/28/09	Mon 6/8/09
16	CAR for Award of Contract	20 days	Mon 6/8/09	Tue 6/30/09
17	Award of Contract	0 days	Tue 6/30/09	Tue 6/30/09
18	Process the Contract	17 days	Tue 6/30/09	Mon 7/20/09
19	Notice to Proceed	0 days	Mon 7/20/09	Mon 7/20/09
20	CONSTRUCTION	250 days	Mon 7/20/09	Mon 4/28/10
21	Pre-Construction Meeting	2 days	Mon 7/20/09	Tue 7/21/09
22	Material Acquisition - land side	20 days	Mon 7/20/09	Tue 8/11/09
23	Construction - land side	40 days	Mon 7/20/09	Wed 9/2/09
24	Contractor Submittals - water side	69 days	Mon 7/20/09	Mon 10/5/09
25	Water Side Approvals including B&S	11 days	Mon 10/5/09	Fri 10/16/09
26	Water Side Fabrication	100 days	Fri 10/16/09	Fri 2/5/10
27	Construction - water side	60 days	Fri 2/5/10	Wed 4/14/10
28	Construction Contingency, Punchlist & Acceptance	10 days	Wed 4/14/10	Mon 4/28/10
29	Construction Complete	0 days	Mon 4/28/10	Mon 4/28/10
30	PROJECT WRAP-UP	71 days	Mon 4/28/10	Tue 7/13/10
31	As-Built Drawings, Quantity Changes & Change Orders	18 days	Mon 4/28/10	Fri 5/14/10
32	CAR For Notice of Completion	13 days	Fri 5/14/10	Fri 5/29/10
33	Final Release Form	40 days	Fri 5/29/10	Tue 7/13/10
34	Project Complete	0 days	Tue 7/13/10	Tue 7/13/10

Project: Project Schedule
 Date: Fri 4/10/09

Task Split: Progress: Milestone:

Summary: Project Summary: External Tasks: External Milestone: Deadline:

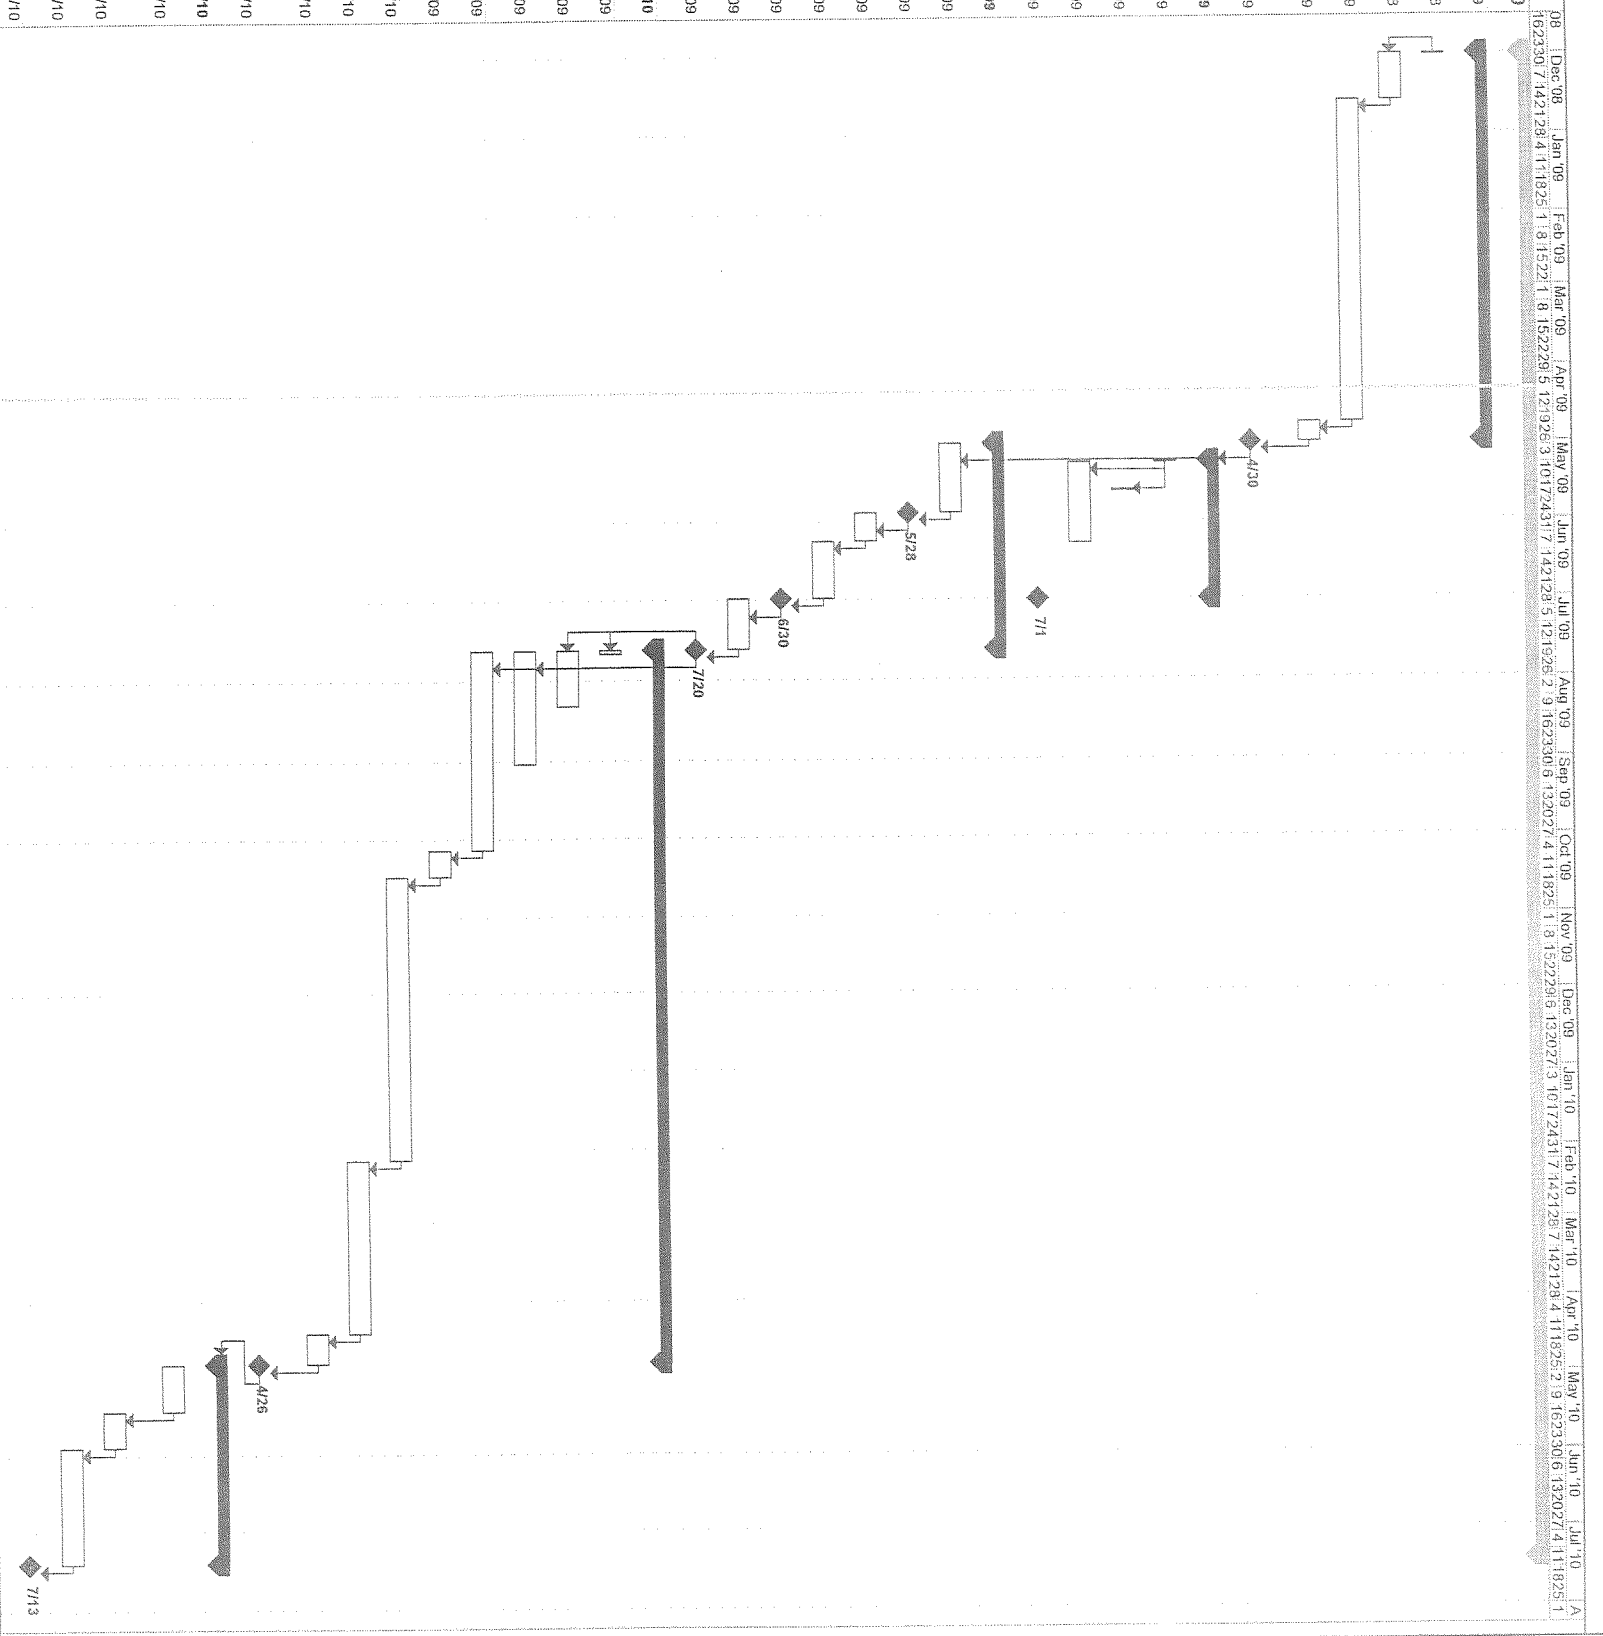

ATTACHMENT #1

MAY 21 2009 #1
