GRANITE™

City of Santa Barbara - Chapala Street
Job # 404922
City of Santa Barbara Project # 7890
3 Week Project Schedule

Project Manager: Matthew Grimm | Start Date: 6/10/2013 | Finish Date: 1/15/2013 | WD: 150 | L/D: 3.000
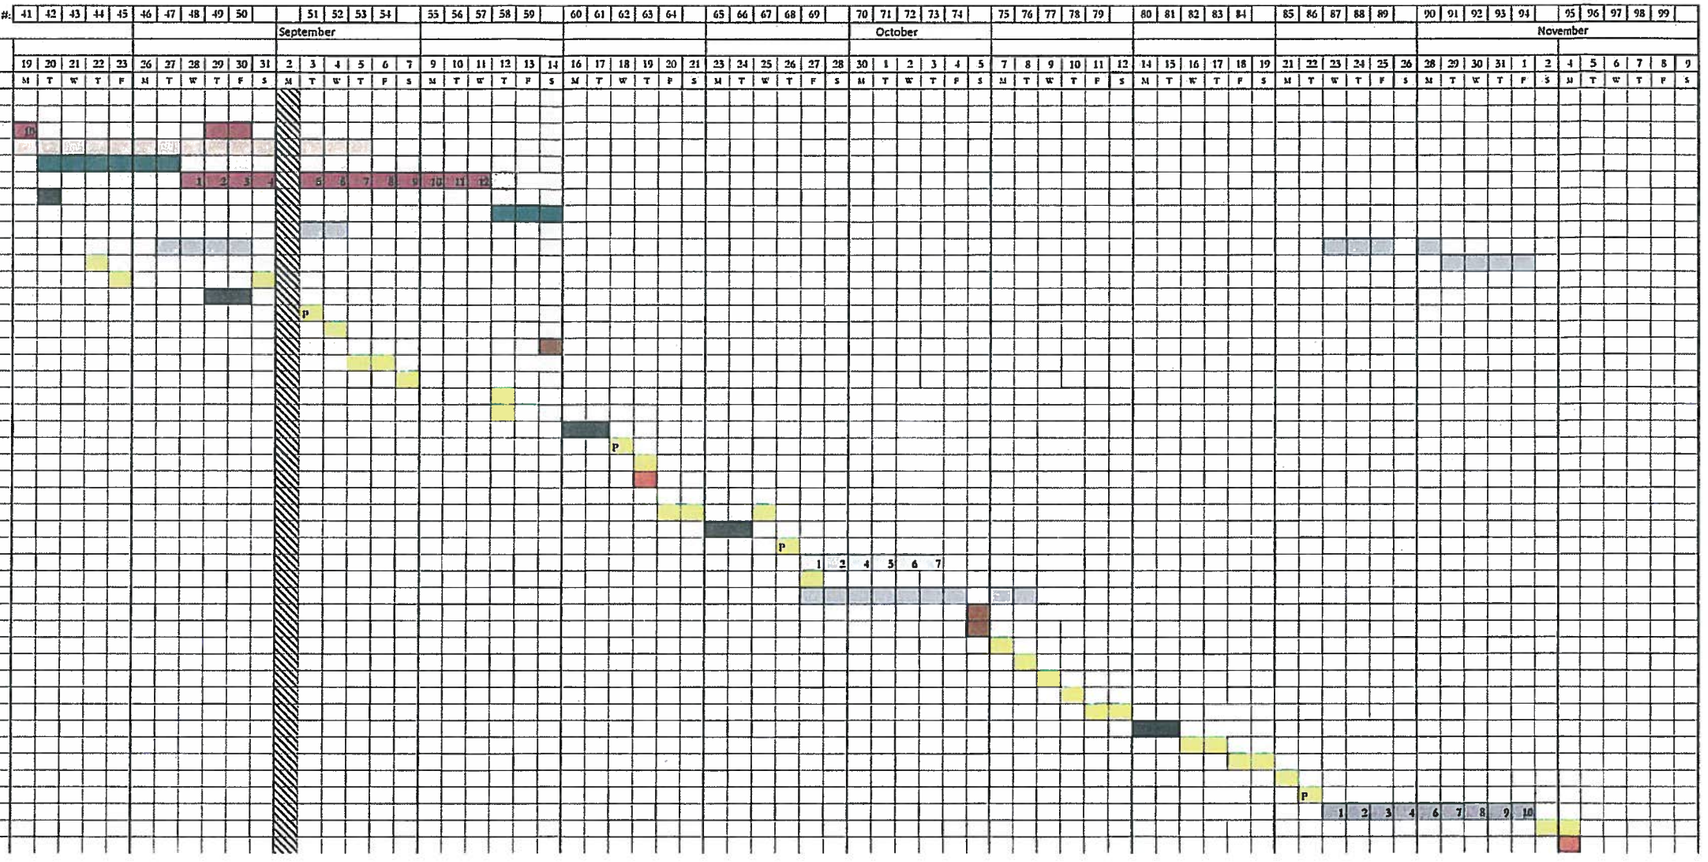
Cost Code	Description	Resp.	Quantity	Days
	CONSTRUCTION			
85050041	Drill 36" CIDH at Abut #2	Mahaffy	530 LF	5
304001	CIDH Drill Support	GCC	11 DY	11
	Acceptence Testing Abut #2 Piles	MNS	530 LF	3
85050040	Drill 24" CIDH at Abut #1	Mahaffy	651 LF	6
85120045	Furnish 24" CIDH Pile Steel	Vista Rebar	651 LF	6
	Acceptence Testing Abut #1 Piles	MNS	651 LF	3
302005	Modify Sand Stone Wall (Front of Abut #2)	GCC	173 SF	4
302005	Modify Sand Stone Wall (ALL)	GCC	416 SF	8
304002	Prep Abut #2 Piles	GCC	70 SF	0.25
304312	Form Abut #2	GCC	724 SF	2
85120045	Install Abut #2 Rebar	Vista Rebar	51 CY	1
304313	Pour Abut #2	GCC	51 CY	1
304312	Strip Abut #2	GCC	724 SF	1
303103	Backfill Abut #2	GCC	52 CY	1
304322	Set F/W Pad at Abut #2	GCC	1 EA	0.5
304323	Build / Erect Bent	GCC	1 EA	1
304002	Prep Abut #1 Piles	GCC	39 SF	0.25
304201	Form Abut #1 Footing	GCC	376 SF	2
85120045	Install Abut #1 Footing Rebar	Vista Rebar	59 CY	2
304202	Pour Abut #1 Footing	GCC	59 CY	1
304201	Strip Abut #1 Footing	GCC	376 SF	0.5
	Install Shoring beams	GCC		0.5
304203	Prep / Sandblast Joint	GCC	84 SF	0.5
304312	Form Abut #1	GCC	1,402 SF	3
85120045	Install Abut #1 Rebar	Vista Rebar	51 CY	2
304313	Pour Abut #1	GCC	51 CY	1
	Cure Abut #1			7
304312	Strip Abut #1	GCC	1,402 SF	1
301805	Reconstruct S.S. Wall	GCC	608 SF	9
	Pull shoring/Backfill	GCC		
304802	Grade for Concrete Lining	GCC	350 SF	0.5
304803	Pour Back Concrete Lining	GCC	4 CY	0.5
304322	Set F/W Pad at Abut #2	GCC	1 EA	0.5
304323	Build / Erect Bent	GCC	1 EA	1
304224	Set Stringers	GCC	15 EA	1
304325	Deck Soffit	GCC	2,930 SF	2
85120045	Install Rebar	Vista Rebar	50,000 LB	2
304333	Form Edge of Deck	GCC	175 SF	1
304326	Grade Falsework	GCC	2,930 SF	1
304334	Set / Grade Rails	GCC	150 LF	1
304336	Place Concrete	GCC	187 CY	1
	Cure Deck		1 LS	10
	Strip Falsework	GCC	2,930 SF	2
	Remove Diversion
